

# 2/26-2/27貴儀測試

- **船速**：風力5-7級



Time	RPM(P) 左車	RPM(S) 右車	SOG 對地(節)	STW 對水(節)
10:00	200	150	8.5	8.8
11:00	200	150	9.0	8.8
12:00	200	150	8.6	8.6
13:00	200	150	8.2	8.2
14:00	200	150	8.3	8.3
15:00	200	150	7.7	7.8

- **USBL**：維修中。水下感測器已更換電源供應器，2/22發生電腦主機燒毀，2/23先與廠商借用備品測試，預計維修後於4月安排測試。

- **CTD**：正常。以率定報告為主

- **XBT**：正常。

1. 2/26施放 1 支T10
2. 2/27施放 2 支T7、1 支T10

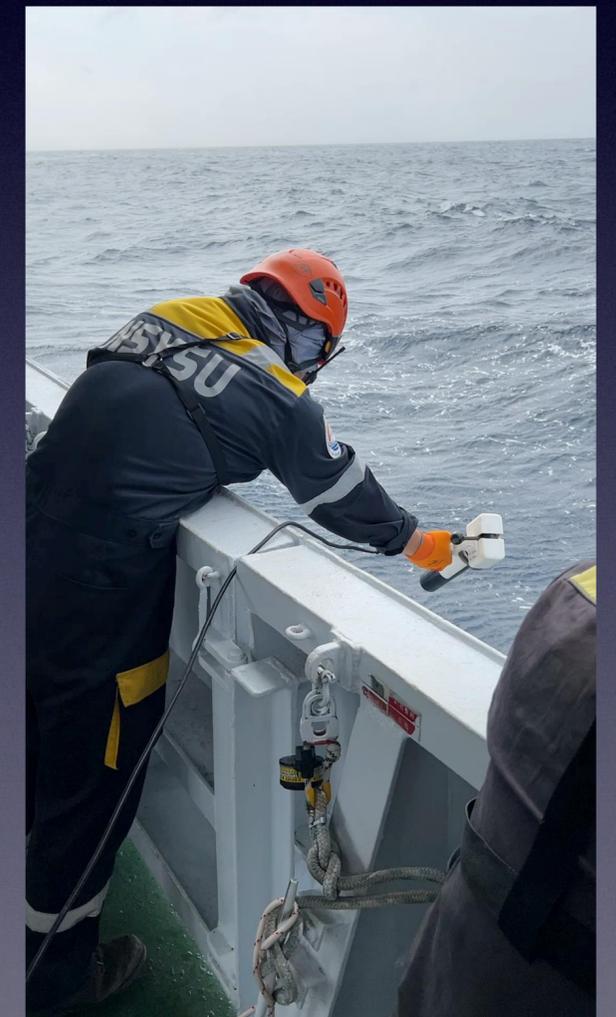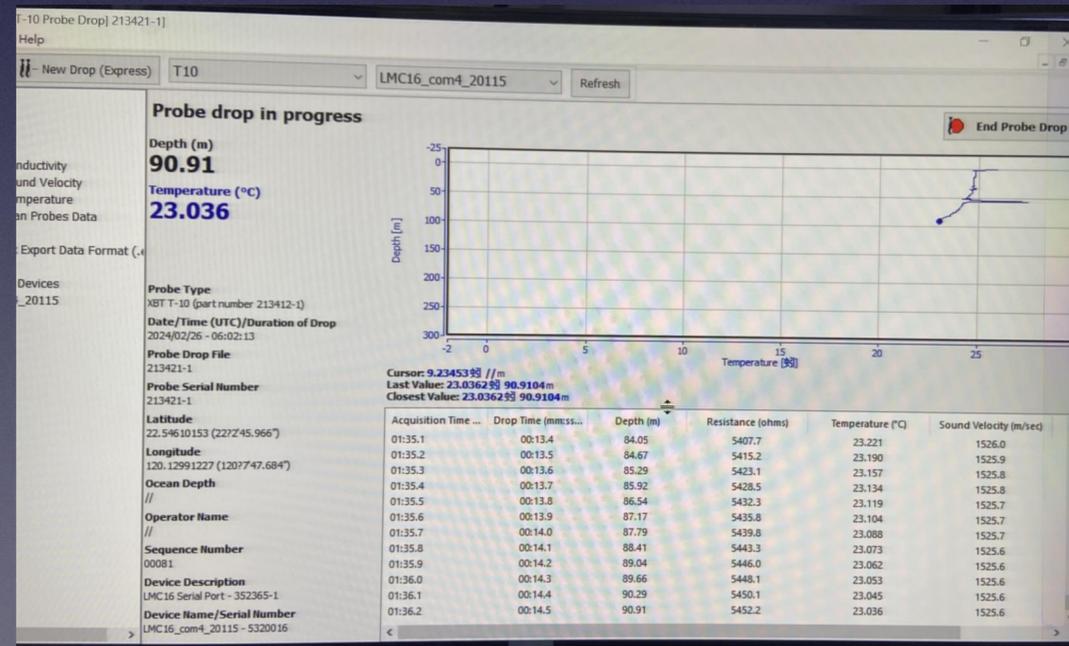

# 2/26-2/27 貴儀測試

- **Box corer** : 施放 3 次



